

Construction Progress Update

New Rochelle School District Energy Project

February 11, 2016

**Construction Progress Update
New Rochelle School District Energy Project
(Honeywell USB-008791)**

Date: February 10, 2015
Location: New Rochelle, NY
Prepared: February 10, 2015
By: Paddy Phelan

Page: 1
of: 5

Purpose: CONSTRUCTION PROGRESS



Construction Kick-off	August 31, 2015
Baseline Completion	April 1, 2016
Adjusted Completion	March 15, 2016
Duration Months	8
Overall Construction Progress	100%

GENERAL GUIDELINES & SAFETY REQUIREMENTS

- In the event of an emergency, please call Paddy Phelan at 516-448-8645.
- All contractors are responsible for maintaining safe work habits and conforming to OSHA Regulations. Any protective clothing or personal protection as required by the task must be worn at all times.
- Honeywell will maintain a Health & Safety Manual on site for the duration of the project.

ECM 1 – Lighting & Occupancy Sensors

Construction Progress Update**New Rochelle School District Energy Project**

February 11, 2016

Building	Start	Finish
New Rochelle High School		Complete 12/30/15
Albert Leonard Middle School		Complete 12/9/15
George M. Davis Elementary School		Complete 10/19/15
Columbus Elementary School		Complete 10/16/15
Trinity Elementary School		Complete 10/30/15
William B. Ward Elementary School		Complete 10/9/15
Daniel Webster Elementary School		Complete 12/2/15
Henry Bernard Elementary School		Complete 11/16/15
Isaac E. Young Middle School		Complete 11/6/15
Jefferson Elementary School		Complete 10/23/15



- Lighting install is complete.

Estimated Completion Date: 12/30/15

Percent Complete: 100%

Construction Progress Update

New Rochelle School District Energy Project

February 11, 2016

ECM 2 – Boiler Replacement

New Boilers

Building	Start	Finish
Albert Leonard Middle School	Complete 11/6/15	



- Boiler Control work to be completed next week

Estimated Completion Date: 11/6/15

Percent Complete: 100%

ECM 3 – Install Boiler Burner Controls

Building	Start	Finish
Henry Bernard Elementary School	Complete 10/28/15	
George M. Davis Elementary School	Complete 11/30/15	
Trinity Elementary School	Complete 12/2/15	
Daniel Webster Elementary School	Complete 12/16/15	
Jefferson Elementary School	Complete 12/22/15	

Estimated Completion Date: 12/22/15

Percent Complete: 100%

Construction Progress Update

New Rochelle School District Energy Project

February 11, 2016

ECM 4 – Install De-stratification Fans

Building	Start	Finish
New Rochelle High School		Complete 12/30/15
Albert Leonard Middle School		Complete 12/15/15
Isaac E. Young Middle School		Complete 12/9/15
Columbus Elementary School		Complete 12/23/16
George M. Davis Elementary School		Complete 12/2/14

Estimated Completion Date: 12/30/15

Percent Complete: 100%

ECM 5 – Walk-in Freezer/Cooler Controls

Building	Start	Finish
New Rochelle High School		Complete 9/25/15
Albert Leonard Middle School		Complete 9/25/15
Isaac E. Young Middle School		Complete 9/24/15
Columbus Elementary School		Complete 9/25/15
Trinity Elementary School		Complete 9/24/15
William B. Ward Elementary School		Complete 9/24/15
Daniel Webster Elementary School		Complete 9/24/15

- Walk-in Freezer and Cooler controls are complete

Estimated Completion Date: 9/25/15

Percent Complete: 100%

ECM 6 – Demand Control Ventilation

Building	Start	Finish
George M. Davis Elementary School		Complete 12/30/15

Estimated Completion Date: 12/30/15

Percent Complete: 100%

Construction Progress Update

New Rochelle School District Energy Project

February 11, 2016

ECM 7 – Plug Load Management


Building	Start	Finish
New Rochelle High School		Complete 12/15/16
Albert Leonard Middle School		Complete 11/22/15
George M. Davis Elementary School		Complete 12/29/15
Trinity Elementary School		Complete 11/19/15
William B. Ward Elementary School		Complete 11/20/15
Isaac E. Young Middle School		Complete 1/28/16

Estimated Completion Date: 1/28/16

Percent Complete: 100%

ECM 8 – Roof Replacement

Building	Start	Finish
Columbus Elementary School		Complete 8/21/15

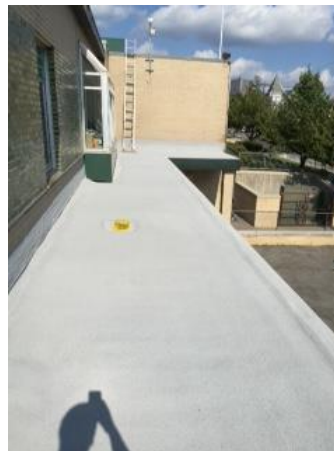

- Roof replacement is complete at Columbus ES

Estimated Completion Date: 10/23/15

Percent Complete: 100%

ECM 9 – Unit Vent Replacement

Construction Progress Update**New Rochelle School District Energy Project**

February 11, 2016

Building	Start	Finish
Columbus Elementary School	Complete 10/23/15	

- Unit Vent install is complete

Estimated Completion Date 10/23/15

Percent Complete: 100%

Number of safe working days: 90**Number of workers onsite: 25**
